

BaBar Event Store

ID	Task Name	Duration	Start	Finish	1998											
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
1	BaBar Event Store	503d	Fri 11/1/96	Thu 10/1/98	[Gantt bar spanning from Q1 1998 to Q4 1998]											
2	API Specifications	56d	Fri 11/1/96	Mon 1/20/97	[Gantt bar from Q1 1997 to Q1 1998]											
3	Low Level API	56d	Fri 11/1/96	Mon 1/20/97	[Gantt bar from Q1 1997 to Q1 1998]											
4	Development	36d	Fri 11/1/96	Fri 12/20/96	[Gantt bar from Q1 1997 to Q1 1998]											
5	Draft out for comments	0d	Fri 12/20/96	Fri 12/20/96	[Gantt bar from Q1 1997 to Q1 1998]											
6	Accepted	0d	Mon 1/20/97	Mon 1/20/97	[Gantt bar from Q1 1997 to Q1 1998]											
7	High Level API	56d	Fri 11/1/96	Mon 1/20/97	[Gantt bar from Q1 1997 to Q1 1998]											
8	Development	36d	Fri 11/1/96	Fri 12/20/96	[Gantt bar from Q1 1997 to Q1 1998]											
9	Draft out for comments	0d	Fri 12/20/96	Fri 12/20/96	[Gantt bar from Q1 1997 to Q1 1998]											
10	Accepted	0d	Mon 1/20/97	Mon 1/20/97	[Gantt bar from Q1 1997 to Q1 1998]											
11	Licensing distribution plan	17d	Thu 1/16/97	Mon 2/10/97	[Gantt bar from Q1 1997 to Q1 1998]											
12	Development	11d	Thu 1/16/97	Thu 1/30/97	[Gantt bar from Q1 1997 to Q1 1998]											
13	Draft out for comments	0d	Fri 1/31/97	Fri 1/31/97	[Gantt bar from Q1 1997 to Q1 1998]											
14	Accepted	0d	Mon 2/10/97	Mon 2/10/97	[Gantt bar from Q1 1997 to Q1 1998]											
15	Version 1.0	167d	Fri 11/1/96	Fri 6/20/97	[Gantt bar from Q1 1997 to Q2 1998]											
16	Input Module	13d	Mon 1/20/97	Wed 2/5/97	[Gantt bar from Q1 1997 to Q1 1998]											
17	Development	13d	Mon 1/20/97	Wed 2/5/97	[Gantt bar from Q1 1997 to Q1 1998]											
18	Available for Release 1.0	0d	Wed 2/5/97	Wed 2/5/97	[Gantt bar from Q1 1997 to Q1 1998]											
19	Output Module	17d	Thu 2/6/97	Fri 2/28/97	[Gantt bar from Q1 1997 to Q1 1998]											
20	Development	17d	Thu 2/6/97	Fri 2/28/97	[Gantt bar from Q1 1997 to Q1 1998]											
21	Available for Release 1.0	0d	Fri 2/28/97	Fri 2/28/97	[Gantt bar from Q1 1997 to Q1 1998]											
22	Schema & Configuration	130d	Fri 11/1/96	Thu 5/1/97	[Gantt bar from Q1 1997 to Q2 1998]											
23	Development	130d	Fri 11/1/96	Thu 5/1/97	[Gantt bar from Q1 1997 to Q2 1998]											
24	Schema & Configuration frozen	0d	Thu 5/1/97	Thu 5/1/97	[Gantt bar from Q1 1997 to Q2 1998]											
25	Demonstration	0d	Thu 5/1/97	Thu 5/1/97	[Gantt bar from Q1 1997 to Q2 1998]											
26	Productizing & validation tests	37d	Fri 5/2/97	Fri 6/20/97	[Gantt bar from Q1 1997 to Q2 1998]											
27	Release	0d	Fri 6/20/97	Fri 6/20/97	[Gantt bar from Q1 1997 to Q2 1998]											
28	Version 2.0	133d	Fri 5/2/97	Mon 11/3/97	[Gantt bar from Q1 1997 to Q2 1998]											
29	Input Module	13d	Fri 5/2/97	Tue 5/20/97	[Gantt bar from Q1 1997 to Q2 1998]											
30	Development	13d	Fri 5/2/97	Tue 5/20/97	[Gantt bar from Q1 1997 to Q2 1998]											
31	Available for Release 2.0	0d	Tue 5/20/97	Tue 5/20/97	[Gantt bar from Q1 1997 to Q2 1998]											


Project: BaBar Event Store Schedule
 Author: David R. Quarrie (DRQuarrie@LBL.Gov)
 Date: Wed 3/26/97

Task
 Progress

Milestone
 Summary

Rolled Up Task
 Rolled Up Milestone

Rolled Up Progress

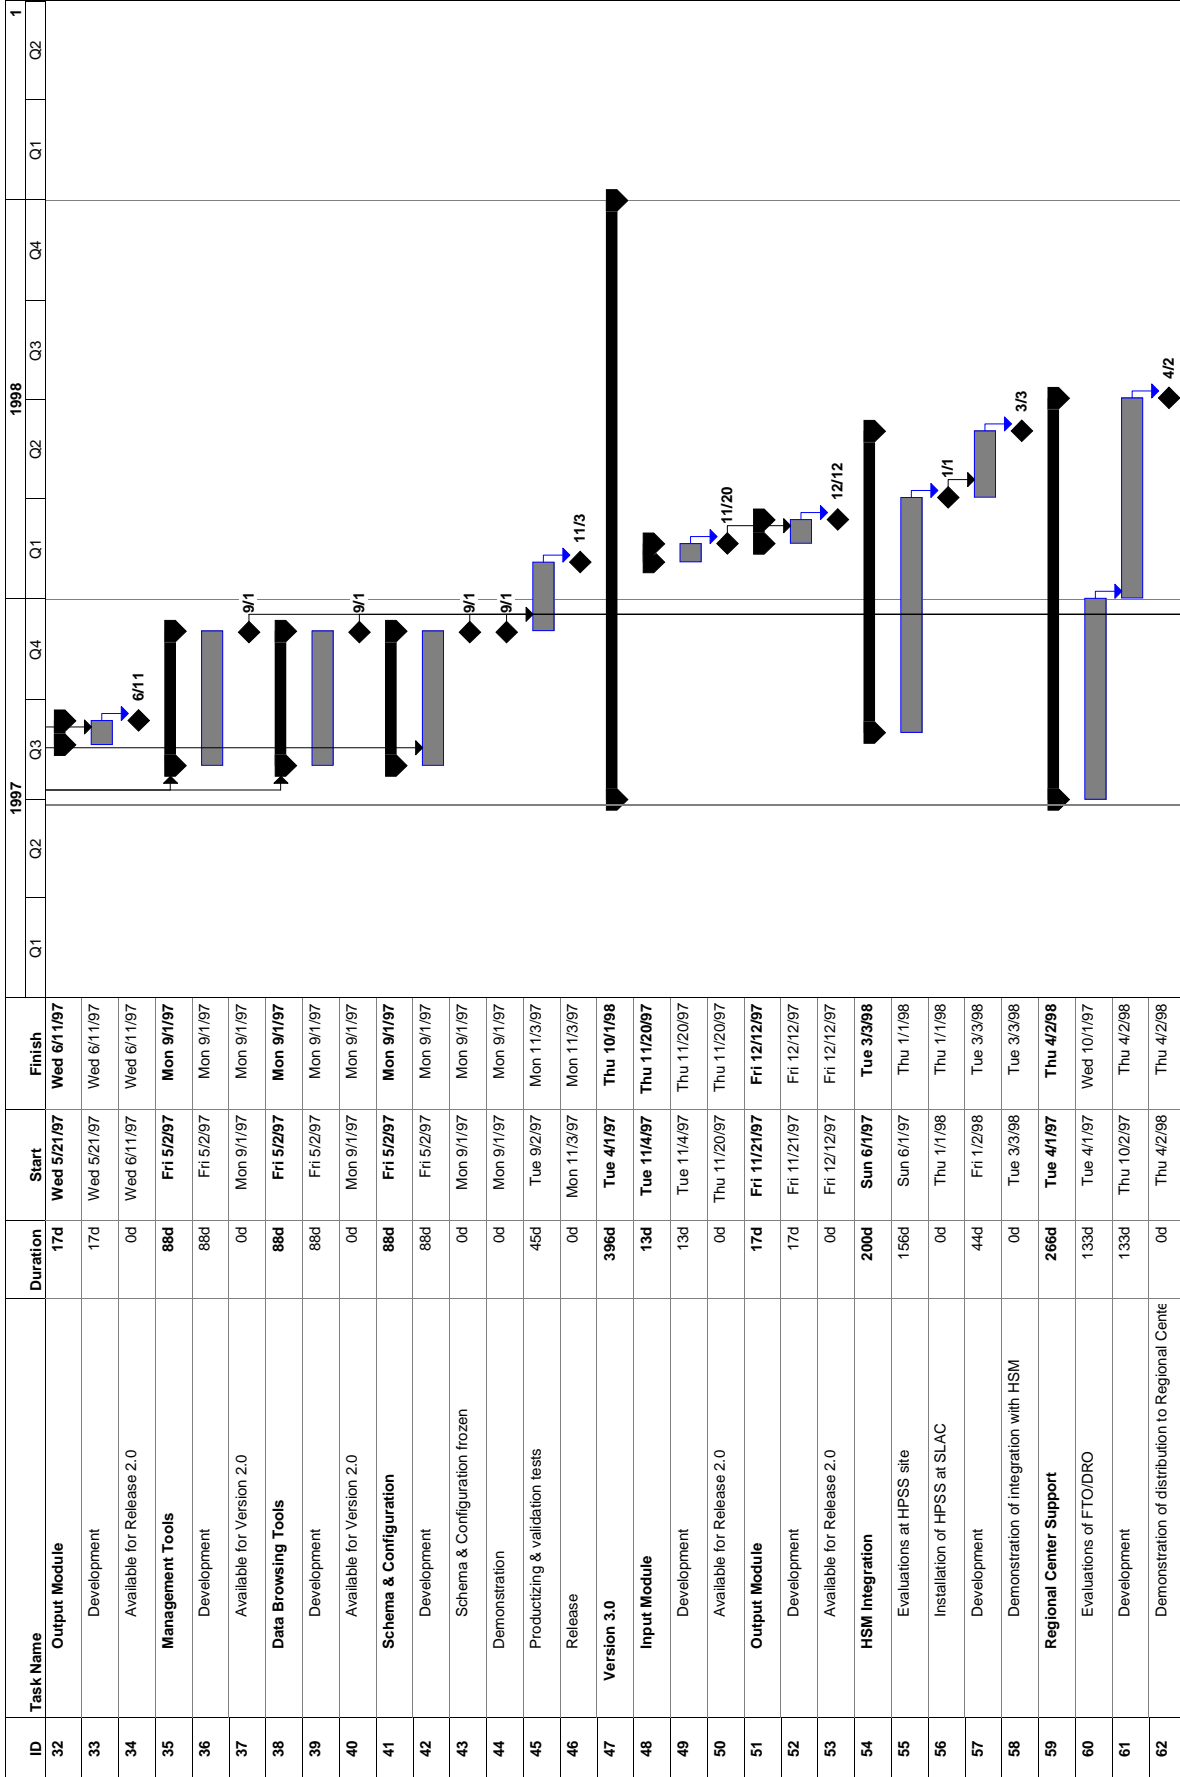

Project: BaBar Event Store Schedule
 Author: David R. Quarrie (DRQuarrie@LBL.Gov)
 Date: Wed 3/26/97

Task
 Progress

Milestone
 Summary

Rolled Up Task
 Rolled Up Milestone

Rolled Up Progress

ID	Task Name	Duration	Start	Finish	1997				1998				1			
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
63	Online Logging	143d	Wed 10/1/97	Wed 4/15/98												
64	Development	143d	Wed 10/1/97	Wed 4/15/98												
65	Demonstration of backup capabilities	0d	Wed 4/15/98	Wed 4/15/98												
66	Management Tools	231d	Mon 9/1/97	Wed 7/15/98												
67	Development	231d	Mon 9/1/97	Wed 7/15/98												
68	Available for Version 3.0	0d	Wed 7/15/98	Wed 7/15/98												
69	Data Browsing Tools	231d	Mon 9/1/97	Wed 7/15/98												
70	Development	231d	Mon 9/1/97	Wed 7/15/98												
71	Available for Version 3.0	0d	Wed 7/15/98	Wed 7/15/98												
72	Access Monitoring Tools	231d	Sun 6/1/97	Wed 4/15/98												
73	Development	231d	Sun 6/1/97	Wed 4/15/98												
74	Available for Version 3.0	0d	Wed 4/15/98	Wed 4/15/98												
75	Schema & Configuration	165d	Mon 9/1/97	Wed 4/15/98												
76	Development	165d	Mon 9/1/97	Wed 4/15/98												
77	Schema & Configuration frozen	0d	Wed 4/15/98	Wed 4/15/98												
78	Release	0d	Wed 4/15/98	Wed 4/15/98												
79	Performance & Scaling tests	122d	Wed 4/15/98	Thu 10/1/98												
80	Tests & Optimizations	122d	Wed 4/15/98	Wed 9/30/98												
81	Performance and Scaling milestones met	0d	Thu 10/1/98	Thu 10/1/98												

Project: BaBar Event Store Schedule
 Author: David R. Quarrie (DRQuarrie@LBL.Gov)
 Date: Wed 3/26/97

Task
 Progress

Milestone
 Summary

◆ Rolled Up Task
 ◊ Rolled Up Milestone

■ Rolled Up Progress
