ID		Task Name	Duration	Start	Finish	Predecessors
1		Upgrade Dataflow to Tornado2 (	4 wks	Mon 7/14/03	Fri 8/8/03	
2	✓	**New BFARCH**	**14 days**	**Wed 5/21/03**	**Mon 6/9/03**	
3	✓	Propose new scheme	3 days	Wed 5/21/03	Fri 5/23/03	
4	✓	Post to Pkg Coords HN	1 day	Mon 5/26/03	Mon 5/26/03	3
5	✓	Update SoftRelTools/SiteCo	2 wks	Tue 5/27/03	Mon 6/9/03	4
6		**Switch Linux Compiler**	**27 days**	**Tue 6/10/03**	**Wed 7/16/03**	
7	✓	Add gcc3 nightly	2 days	Tue 6/10/03	Wed 6/11/03	5
8		**IOStreams Migration**	**27 days**	**Tue 6/10/03**	**Wed 7/16/03**	
9		Develop iostreams mi	9 days	Tue 6/10/03	Fri 6/20/03	
10		Migrate nightly/13.7.0	10 days	Mon 6/23/03	Fri 7/11/03	9,36SS
11		Regression test	1 day	Mon 7/14/03	Mon 7/14/03	10
12		Migrate online packag	3 days	Mon 7/14/03	Wed 7/16/03	10
13		**Switch Linux OS to RedHat9**	**44 days**	**Thu 5/22/03**	**Tue 7/22/03**	
14	✓	Obtain RH9 Machines from	3 wks	Tue 5/27/03	Mon 6/16/03	
15		**Validate RH72 Executable**	**3 days**	**Tue 6/17/03**	**Thu 6/19/03**	
16	✓	Prompt Reconstructio	1 day	Tue 6/17/03	Tue 6/17/03	14
17	✓	Simulation Production	1 day	Wed 6/18/03	Wed 6/18/03	14,16
18		Analysis	1 day	Thu 6/19/03	Thu 6/19/03	14,17
19	✓	Install RH9 at IR-2	2.5 days	Thu 5/22/03	Mon 5/26/03	
20		Validate RH72 Online	2 days	Mon 5/26/03	Wed 5/28/03	19
21		Build with gcc 2.95.3 on RH	5 days	Tue 6/17/03	Mon 6/23/03	14
22		Test PR/SP/Beta	2 days	Tue 6/24/03	Wed 6/25/03	21
23		Test PR/SP/Beta built with g	2 days	Mon 6/30/03	Tue 7/1/03	36
24		Online gcc3 build	1 day	Mon 7/21/03	Mon 7/21/03	38
25		Test online build	1 day	Tue 7/22/03	Tue 7/22/03	24
26		**Solaris 9 Migration**	**22.6 days**	**Tue 5/27/03**	**Thu 6/26/03**	
27		Obtain Solaris9 machine in	3 wks	Tue 5/27/03	Mon 6/16/03	
28		**Validate Solaris8 Executab**	**3 days**	**Fri 6/20/03**	**Tue 6/24/03**	**15**
29		Prompt Reconstructio	1 day	Fri 6/20/03	Fri 6/20/03	27
30		Simulation Production	1 day	Mon 6/23/03	Mon 6/23/03	27,29
31		Analysis	1 day	Tue 6/24/03	Tue 6/24/03	27,30
32		Add Forte7 nightly	2.6 days	Tue 6/17/03	Thu 6/19/03	27
33		Fix nightly build	1 wk	Thu 6/19/03	Thu 6/26/03	32
34		**Development Releases**	**25 days**	**Mon 5/26/03**	**Fri 6/27/03**	
35		13.6.0	5 days	Mon 5/26/03	Fri 5/30/03	
36		13.7.0	5 days	Mon 6/23/03	Fri 6/27/03	
37		**Production Releases**	**40 days**	**Mon 7/14/03**	**Fri 9/5/03**	
38		14.0.0	5 days	Mon 7/14/03	Fri 7/18/03	
39		14.1.0	5 days	Mon 8/11/03	Fri 8/15/03	
40		14.2.0	5 days	Mon 9/1/03	Fri 9/5/03	
41		**PreProduction Activities**	**150 days**	**Mon 6/2/03**	**Fri 12/26/03**	
42		PR Test with 13.6.0-roo-X	35 days	Mon 6/2/03	Fri 7/18/03	35
43		PR Test with 14.0.0	1 mon	Mon 7/21/03	Fri 8/15/03	38,42
44		PR Test with 14.1.0	15 days	Mon 8/18/03	Fri 9/5/03	39,43
45		SP6 Testing 13.6.0-roo-X	35 days	Mon 6/2/03	Fri 7/18/03	35
46		SP6 Testing 14.0.0	1 mon	Mon 7/21/03	Fri 8/15/03	38,45
47		SP6 Testing 14.1.0	15 days	Mon 8/18/03	Fri 9/5/03	39,46
48		SP6 Testing 14.2.0+	4 mons	Mon 9/8/03	Fri 12/26/03	40,47
49		**Production Activities**	**353 days**	**Wed 5/21/03**	**Fri 9/24/04**	
50		Prompt Reconstruction	11.5 mons	Mon 9/8/03	Fri 7/23/04	40
51		Reprocess First 3 months F	3 mons	Mon 1/5/04	Fri 3/26/04	
52		SP5	7 mons	Wed 5/21/03	Tue 12/2/03	
53		SP5 Signal	7 mons	Mon 1/5/04	Fri 7/16/04	
54		SP6	7 mons	Mon 1/5/04	Fri 7/16/04	48
55		"Kanga" Conversion	4 mons	Mon 9/1/03	Fri 12/19/03	
56		Oct Skim	3 mons	Mon 10/6/03	Fri 12/26/03	
57		Jan Skim	3 mons	Mon 1/5/04	Fri 3/26/04	
58		Apr Skim	3 mons	Mon 4/5/04	Fri 6/25/04	
59		Jul Skim	3 mons	Mon 7/5/04	Fri 9/24/04	
60		Most Objy Services Shutdow	1 day	Wed 3/31/04	Wed 3/31/04	55
61		**Major Meetings**	**26 days**	**Fri 6/6/03**	**Fri 7/11/03**	
62		External Computing Review	1 day	Fri 6/6/03	Fri 6/6/03	
63		External Computing Review	2 days	Mon 6/9/03	Tue 6/10/03	
64		CM2 Implementation Works	2 days	Mon 6/23/03	Tue 6/24/03	
65		July Collaboration Meeting	4 days	Tue 7/8/03	Fri 7/11/03	

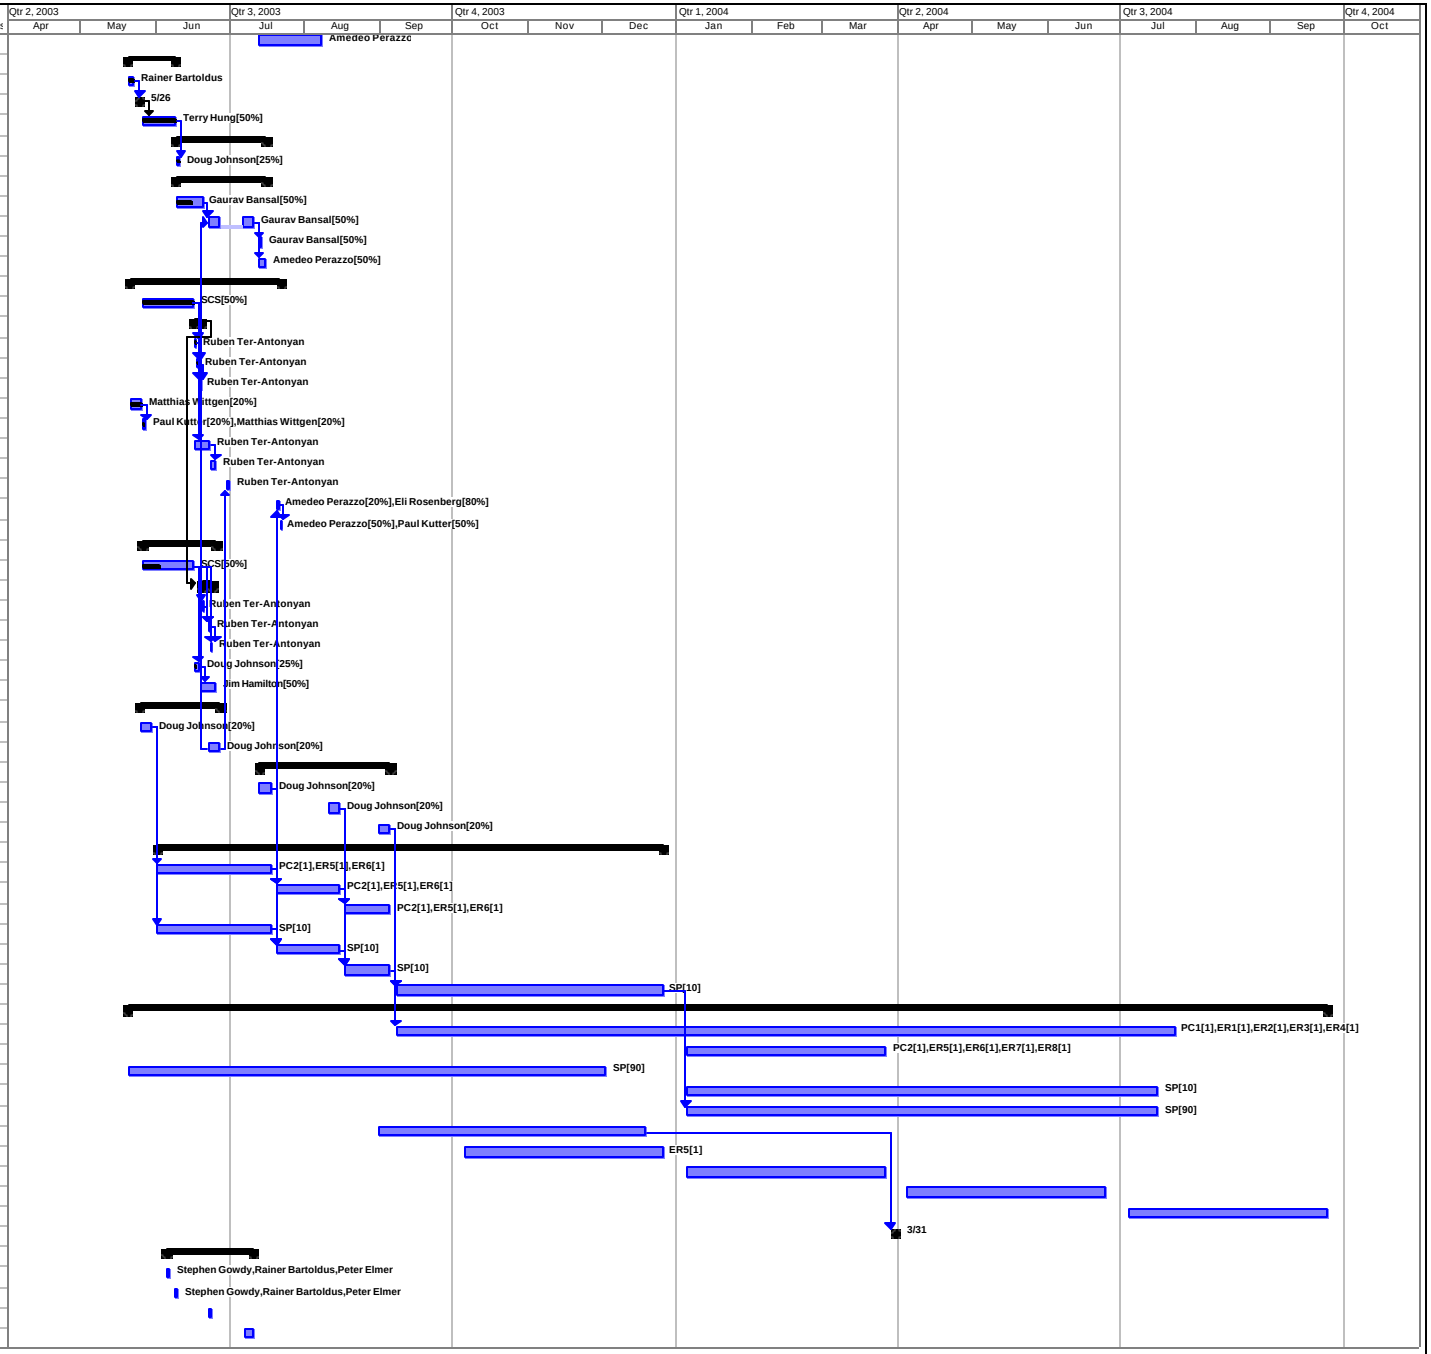

Project: Run4
Date: Thu 6/26/03

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
